



GEORGINA

Multi-Use Recreation Complex Council Update March 1, 2023



Status:

- Structural Steel fully up.
- Gymnasium, discover branch library and lobby roofs near complete, pool in progress.
- Siding progressing well.
- Electrical and mechanical progressing well.
- Pool mechanical progressing well.
- Slab concrete pour for Aquatics change and lobby complete.
- Pool area masonry progressing well.

- Camera updates every 15 minutes at the link below.

<https://timelapse.stealthmonitoring.com/aquicongeorgina/>



Schedule:

- ~~56%~~ 60% complete by cost
 - Current schedule is targeting Q4 2023 turn over to the Town to outfit with furniture and equipment.
 - Target open to public Q1 2024.
-



MURC Site Capital Project Budget:

- Project Budget \$50.2M
 - Forecasting to be delivered within the approved budget.
-





January 31, 2023





February 27, 2022






View of Lobby





View of Gymnasium

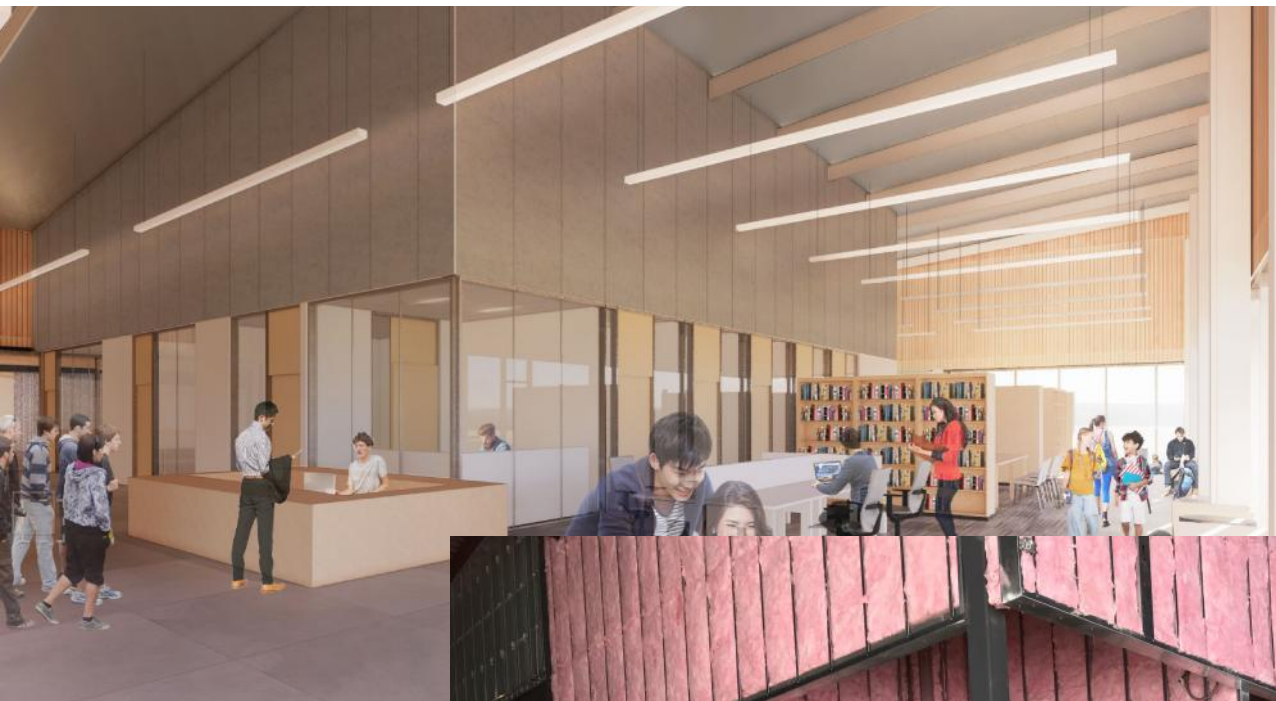


View of Discovery Branch Library



View of Pool



Electrical room, incoming water room

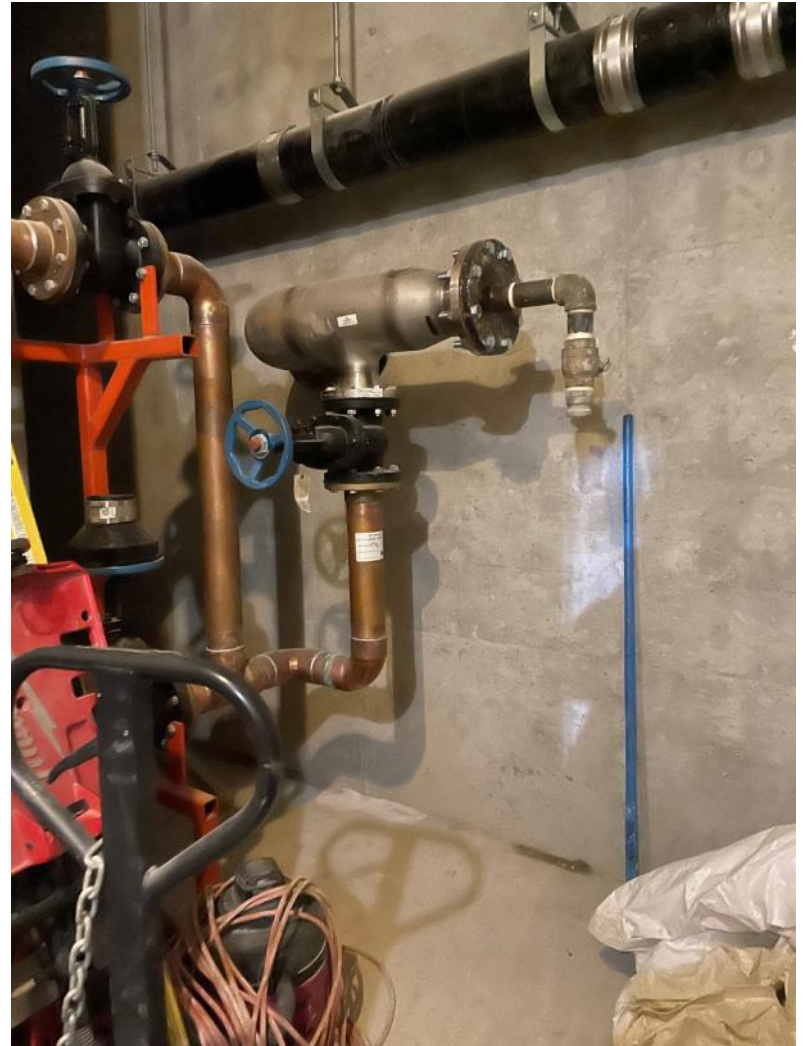



Pool Mechanical





Exterior- North - East



Exterior- South - East



Exterior- South - West



Exterior- North - West

Next Steps:

- Complete roofing.
- Continue with building envelope (including siding and glass).
- Continue with mechanical, electrical and pool mechanical.
- Landscape and pavement. (Summer)
- Interior finishes & fixtures.
- Furniture, Fixtures and Equipment Procurement.
- Planning for commissioning and turn over.

