



GEORGINA

Multi-Use Recreation Complex Council Update June 14, 2023

**Status:**

- Siding progressing.
- Electrical and mechanical progressing well. Major mechanical installed.
- Second water tight tests of all 3 pools is complete. Tiling has started.
- Interior glass curtain wall frames being installed.
- Walking track railing nearing completion.
- Landscape started. Most curbs and planters complete.
- Fireplace unit arrived on site.
- Ceilings in pool and library painted.

Camera updates every 15 minutes at the link below.

<https://timelapse.stealthmonitoring.com/aquicongeorgina/>



Schedule:

- Estimated 71% complete by cost.
 - Current schedule is targeting Q4 2023 turn over to the Town to outfit with furniture and equipment.
 - Target open to public Q1 2024.
-



MURC Site Capital Project Budget:

- Project Budget \$50.2M
 - Forecasting to be delivered within the approved budget.
-





May 1, 2023





June 6, 2023






View of Lobby






View of Gymnasium



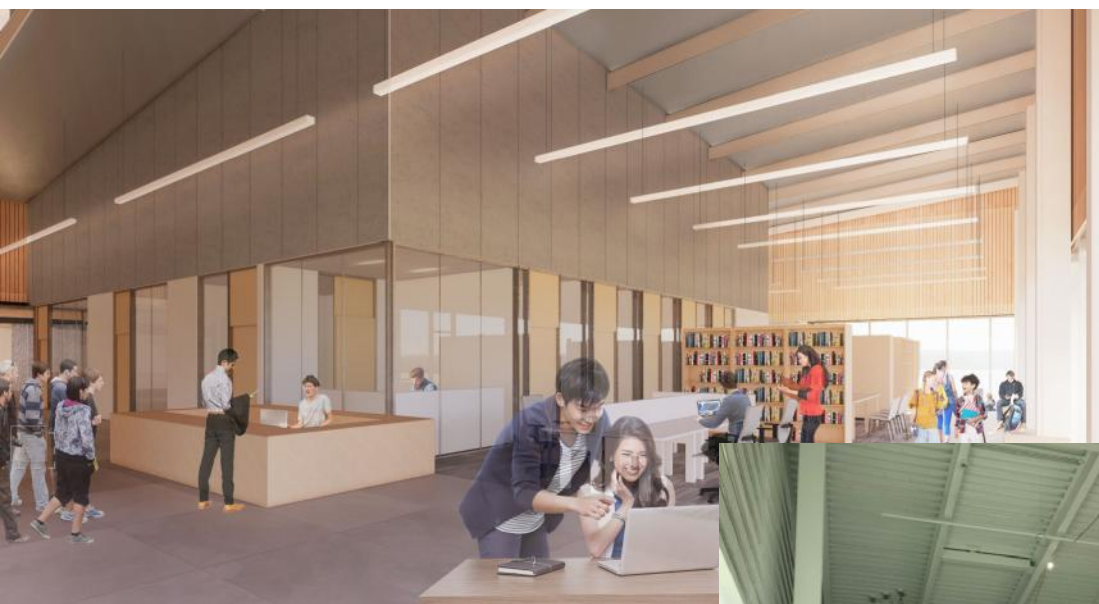

View of Discovery Branch Library

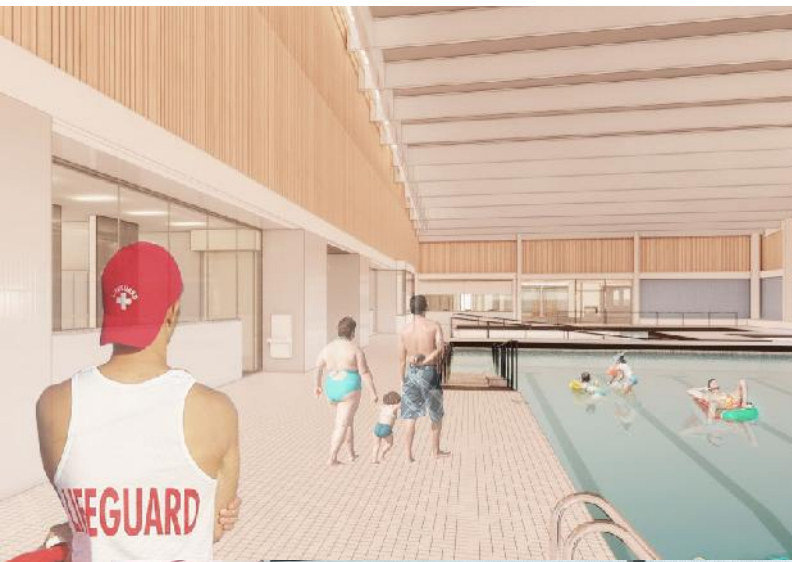

View of Pool





Incoming electrical in progress



Exterior- North



Exterior- South - East



Exterior- North - West

Next Steps:

- Continue with building envelope (including siding and glass).
- Continue with mechanical, electrical and pool mechanical.
- Landscape and pavement.
- Interior finishes & fixtures.
- Furniture, Fixtures and Equipment Procurement.
- Planning for commissioning and turn over.



Other items:

-) 820m Multi – Use Path (MUP) on the West side of Woodbine between Glenwoods Avenue and the new MURC
-) Partnership between York Region and the Town of Georgina

