



GEORGINA

Multi-Use Recreation Complex Council Update August 2, 2023



Status:

- Siding nearly complete.
- Electrical and mechanical progressing well. Major mechanical installed.
- Pool tiling almost complete. Grouting has started.
- Interior glass being installed.
- Walking track railing nearing completion.
- Most curbs, planters and walkways complete. Parking lot in progress.
- Fireplace unit and masonry installed.
- Ceilings in gymnasium painted, lighting and speakers being installed.
- Washroom tile nearing completion.

Camera updates every 15 minutes at the link below.

<https://timelapse.stealthmonitoring.com/aquicongeorgina/>



Schedule:

- Estimated 80% complete by cost.
 - Current schedule is targeting Q4 2023 turn over to the Town to outfit with furniture and equipment.
 - Target open to public Q1 2024.
-



MURC Site Capital Project Budget:

- Project Budget \$50.2M
 - Forecasting to be delivered within the approved budget.
-





June 6, 2023





August 1, 2023





View of Lobby




View of Gymnasium



View of Discovery Branch Library



View of Pool

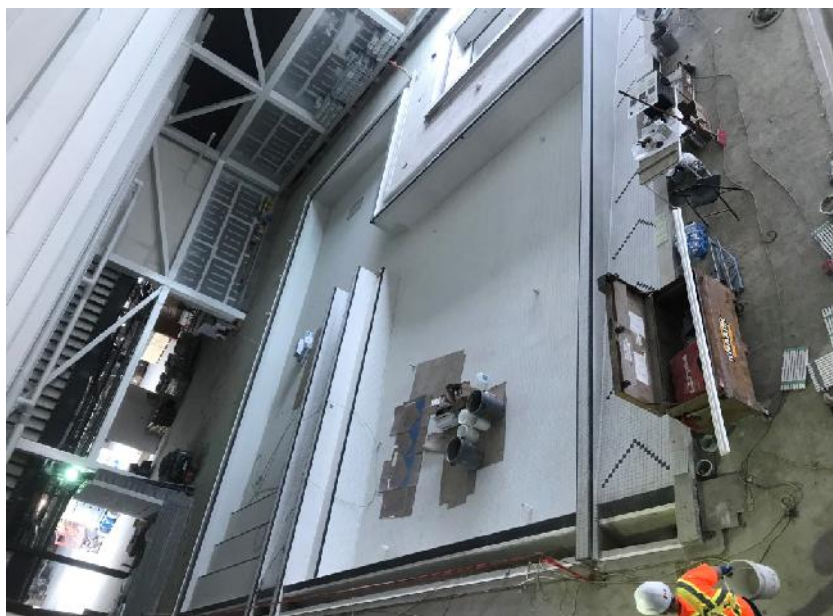



Incoming electrical in progress





Exterior- North



Exterior- South - East



Exterior- North - West

Next Steps:

- Continue with building envelope (including siding and glass).
- Continue with mechanical, electrical and pool mechanical.
- Landscape and pavement.
- Interior finishes & fixtures.
- Furniture, Fixtures and Equipment Procurement.
- Planning for commissioning and turn over.

