



GEORGINA

Multi-Use Recreation Complex Council Update September 20, 2023

**Status:**

- Electrical and mechanical progressing well. Major mechanical installed.
- Pool tiling complete. Changerooms in progress.
- Interior glass mostly installed.
- Walking track railing complete.
- Most walkways complete. Paving in early October.
- Pool and gymnasium lighting and speakers installed.
- Millwork install in progress.
- Many wall finishes in progress or completed.
- Landscape and topsoil spreading in progress.

Camera updates every 15 minutes at the link below.

<https://timelapse.stealthmonitoring.com/aquicongeorgina/>



Schedule:

- Estimated 84% complete by cost at end of August.
 - Current schedule is targeting Q4 2023 turn over to the Town.
 - Target open to public Q1 2024.
-



MURC Site Capital Project Budget:

- Project Budget \$50.2M
 - Forecasting to be delivered within the approved budget.
-





August 1, 2023





September 18, 2023







View of Lobby



View of Gymnasium

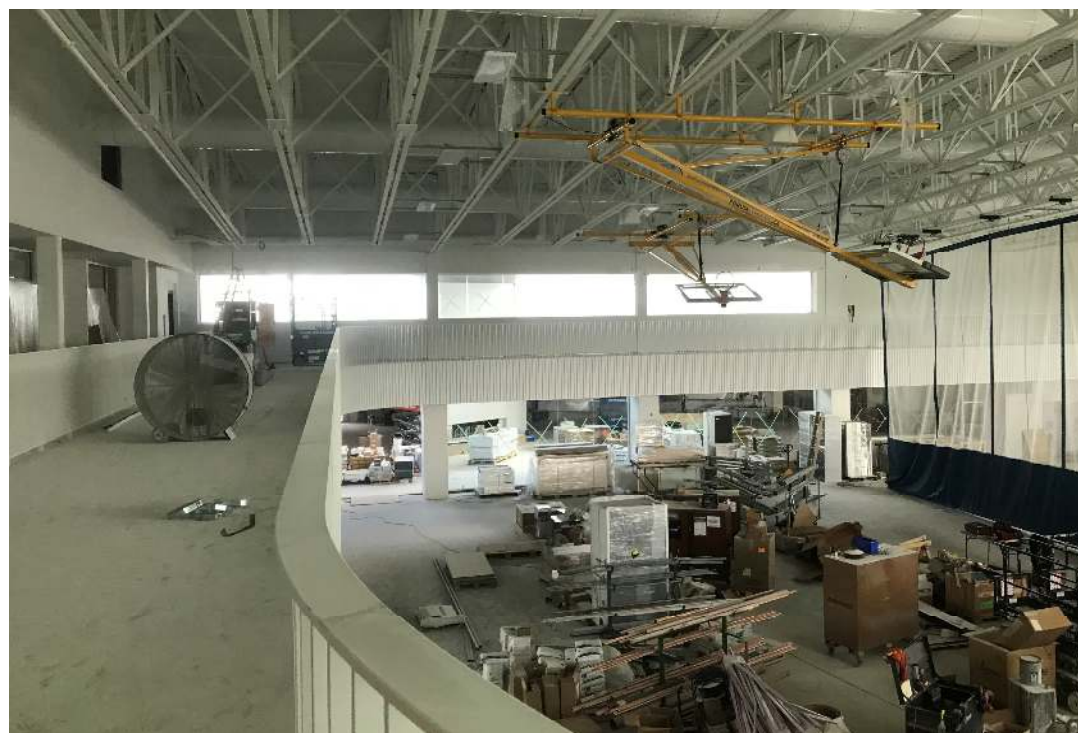

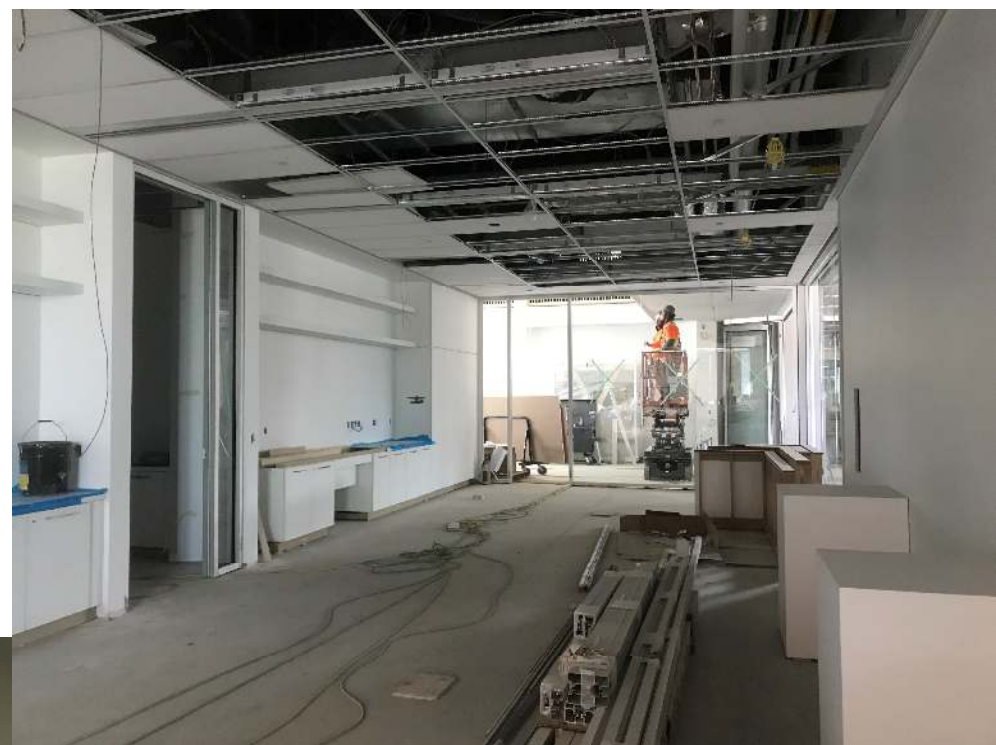

View of Discovery Branch Library



View of Pool



Exterior- North



Exterior- South - East



Exterior- West

Next Steps:

- Continue with building envelope (including glass and tie ins).
- Continue with mechanical, electrical and pool mechanical.
- Landscape and Asphalt.
- Interior finishes & fixtures.
- Furniture, Fixtures and Equipment Procurement.
- Planning for commissioning and turn over.

