



GEORGINA

Multi-Use Recreation Complex Council Update November 8, 2023

**Status:**

- Electrical energized. Mechanical units flushed and starting up.
- Remaining pool deck tiling in progress.
- Interior glass mostly installed.
- Paving and much of the landscape completed.
- Millwork install still in progress.
- Many wall and ceiling finishes in progress or completed.
- Gym flooring has commenced.

Camera no longer updates. Time lapse video coming soon.



Schedule:

- Estimated 92% complete by cost at end of October.
 - December 2023 turn over to the Town.
 - Open to public March 2024.
-




MURC Site Capital Project Budget:

- Project Budget \$50.2M
 - Forecasting to be delivered within the approved budget.
-






View of Lobby

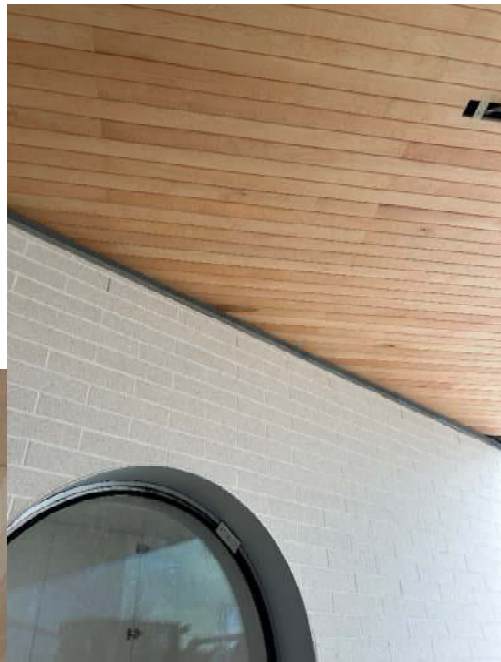



View of Gymnasium

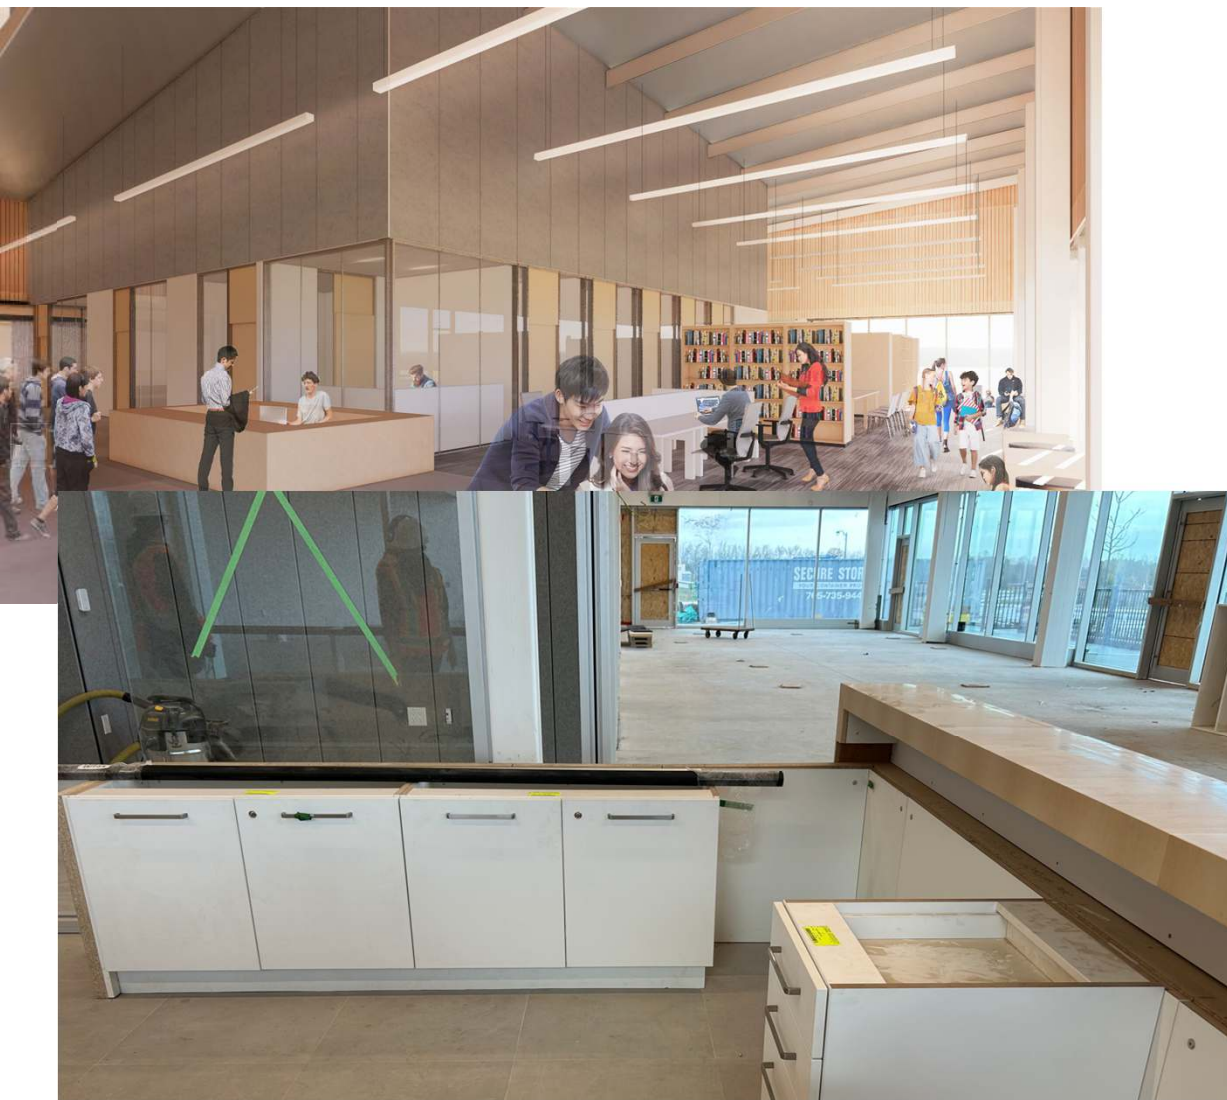

View of Discovery Branch Library



View of Pool





Exterior- Landscape





Exterior- North



Exterior- North - West



Exterior- North





Exterior- South and south east

Next Steps:

- Continue with mechanical, electrical.
- Landscape.
- Interior finishes & fixtures.
- Equipment Procurement.
- Fire Alarm verification.
- Commissioning, testing, balancing, training and turn over.





September 18, 2023





Mid October, 2023

